San Marcos Consolidated Independent School District

Construction Update Hernandez Elementary School – Re-Roof




San Marcos CISD Board Meeting October 15, 2018



Activity Briefing

Completed Activity:

- Completed installation of roof huggers and insulation on building B.
- Completing the installation of soffit, fascia, gutter, and trim on building D.
- Began installing roof panels on building D.
- Began installing fascia panels on building C
- Began installing edge nailer on building C
- Completed canopy E1 panel installation
- Completed canopy H panel installation

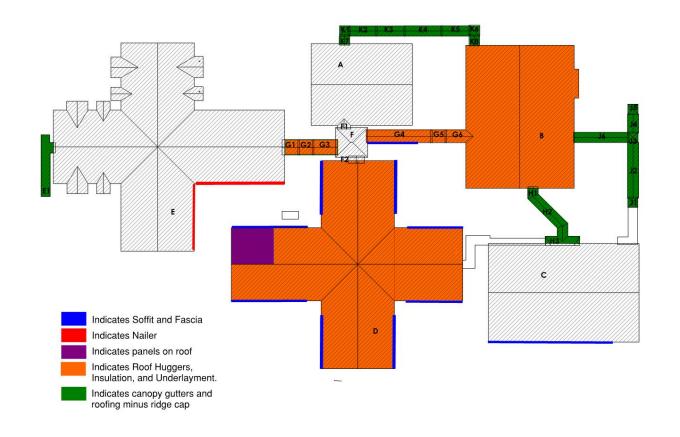






Description: Installation of roof panels on building D



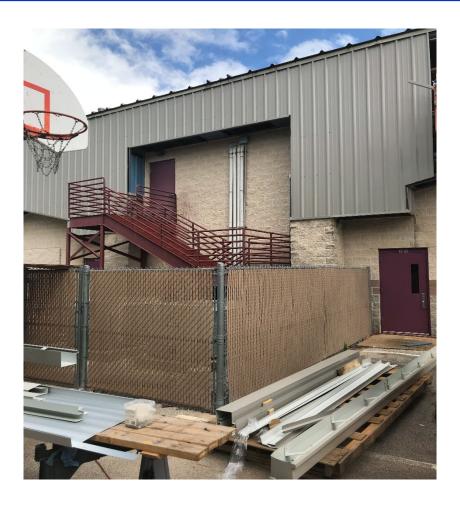

Description: Installation of fascia on building C





Description: Completion of canopy H panels.





Description: Installation of soffit and fascia on building D





Description: Installation of insulation, roof huggers, and soffits on corridor G.



Work Tasks Prior to 11/10/18:

- Completion of roof panel installation on building D.
- Continuation of roof panels on corridor G and building B.
- Begin installing edge nailer, roof huggers and insulation on building A.
- Completion of fascia and soffits on building C.
- Completion of fascia and soffits on corridor G.
- Demolition of fascia and soffits on building B.
- Installation of fascia and soffits on building B.





